Wire list

Aft Fuselage Wiring — Aft Cargo Wiring

Aft Cargo and Tail Cone Wiring — Bulkhead Penetrations and Ground Points

Object code	DMC-ZPH-A-92-41-11-00A-057A-A	**Issue**	001-00 (new)
Issue date	1991-02-16	**Language**	en-GB
Responsible partner	AERALIS S.A.S. (U8025)	**Originator**	AERALIS S.A.S. — Technical Publications, Neuhafen (U8025)
Security	01 — Unclassified	**Quality assurance**	First verification (tabtop)
Applicability	ZEPHYR Family, all aircraft		

Wire list

WIRE No.	GAUGE	TYPE	FROM	TO	LENGTH
4110VC-A01	20	FEP-S	4110VC-A01	4118VC-01	8.40 m
4118VC-B02	20	FEP	4118VC-B02	4110VC-08	2.00 m
4110VC-C03	20	FEP	4110VC-C03	4118VC-15	9.30 m
4118VC-D04	16	FEP	4118VC-D04	4110VC-22	10.30 m
4110VC-A05	22	FEP	4110VC-A05	4118VC-29	10.10 m
4118VC-B06	24	FEP-S	4118VC-B06	4110VC-36	4.70 m
4110VC-C07	22	FEP	4110VC-C07	4118VC-43	3.40 m
4118VC-D08	22	FEP	4118VC-D08	4110VC-02	9.60 m
4110VC-A09	16	FEP	4110VC-A09	4118VC-09	5.50 m
4118VC-B10	14	FEP	4118VC-B10	4110VC-16	7.40 m
4110VC-C11	22	FEP-S	4110VC-C11	4118VC-23	7.00 m
4118VC-D12	24	FEP	4118VC-D12	4110VC-30	6.80 m
4110VC-A13	24	FEP	4110VC-A13	4118VC-37	1.50 m
4118VC-B14	24	FEP	4118VC-B14	4110VC-44	10.20 m
4110VC-C15	16	FEP	4110VC-C15	4118VC-03	9.80 m
4118VC-D16	20	FEP-S	4118VC-D16	4110VC-10	7.80 m
4110VC-A17	18	FEP	4110VC-A17	4118VC-17	7.80 m
4118VC-B18	12	FEP	4118VC-B18	4110VC-24	10.20 m

Harness list

HARNESS	DESIGNATION	ZONE
4110W	GROUND STUD, AFT FUSELAGE WIRING, FWD	143
4111W	BACKSHELL, AFT FUSELAGE WIRING, FWD	146
4118W	CONTACTOR, AFT FUSELAGE WIRING, RH	193

Connector list

CONNECTOR	DESIGNATION	PART NUMBER	CONTACTS

Connector list

CONNECTOR	DESIGNATION	PART NUMBER	CONTACTS
4110VC	BACKSHELL, AFT FUSELAGE WIRING, FWD	D9241009067602	41
4118VC	GROUND STUD, AFT FUSELAGE WIRING, FWD	MOD18630-43	19

Table 1 Equipment on this sheet

FIN	Description	Zone
239VC	GROUND STUD, AFT FUSELAGE WIRING, FWD	193
5VU	BACKSHELL, AFT FUSELAGE WIRING, FWD	146
5792VU3	CONTACTOR, AFT FUSELAGE WIRING, RH	143


This sheet shows the aft cargo compartment and tail cone wiring, with particular emphasis on the rear pressure bulkhead penetrations and the ground point positions behind the bulkhead.

The sheet is drawn looking aft from the aft cargo compartment with the ceiling lining removed. Every penetration of the rear pressure bulkhead is numbered and each carries a pressure seal whose part number is on sheet 2; a penetration disturbed during structural work must have its seal renewed rather than reused. The smoke detection sampling harness is shown dashed because it is routed with the sampling tube and must keep its stated separation from the power runs.

The harness enters the aft cargo compartment at the forward bulkhead, runs aft along the ceiling in zones 143 and 146, and passes through the rear pressure bulkhead at penetrations 4, 7 and 11 into the tail cone in zone 193. Ground points are located on the bulkhead stiffeners immediately aft of the penetrations. Minimum separation between the smoke detection sampling harness and any power run is 60 millimetres. No harness may be attached to a radial segment of the bulkhead web itself.

Bracket stations 4110W-B2, 4111W-B6 and 4118W-B3 carry the harness across the stabiliser attachment fitting area. A bracket station disturbed by structural work must be re-supported and not re-clipped to the nearest surviving station; no re-support scheme is published for any of the three.

Routing: Aft cargo compartment forward bulkhead aft along the ceiling through zones 143 and 146; Rear pressure bulkhead penetrations 4, 7 and 11 into the tail cone in zone 193.

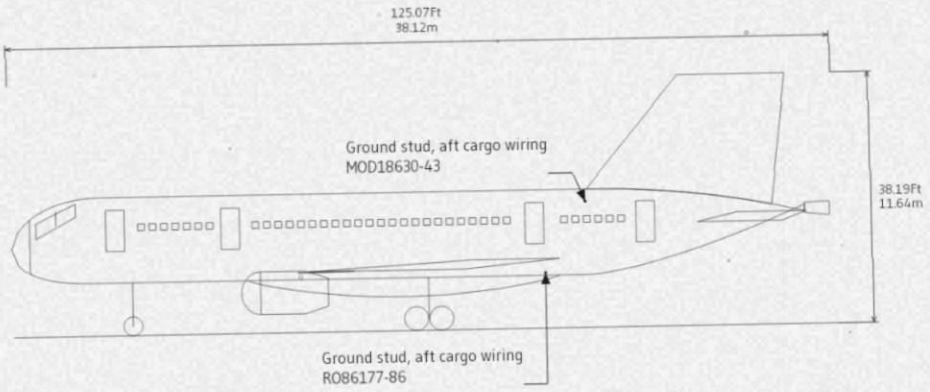

Aft Fuselage Wiring — Aft Cargo Wiring — location, side view — Figure 1
